





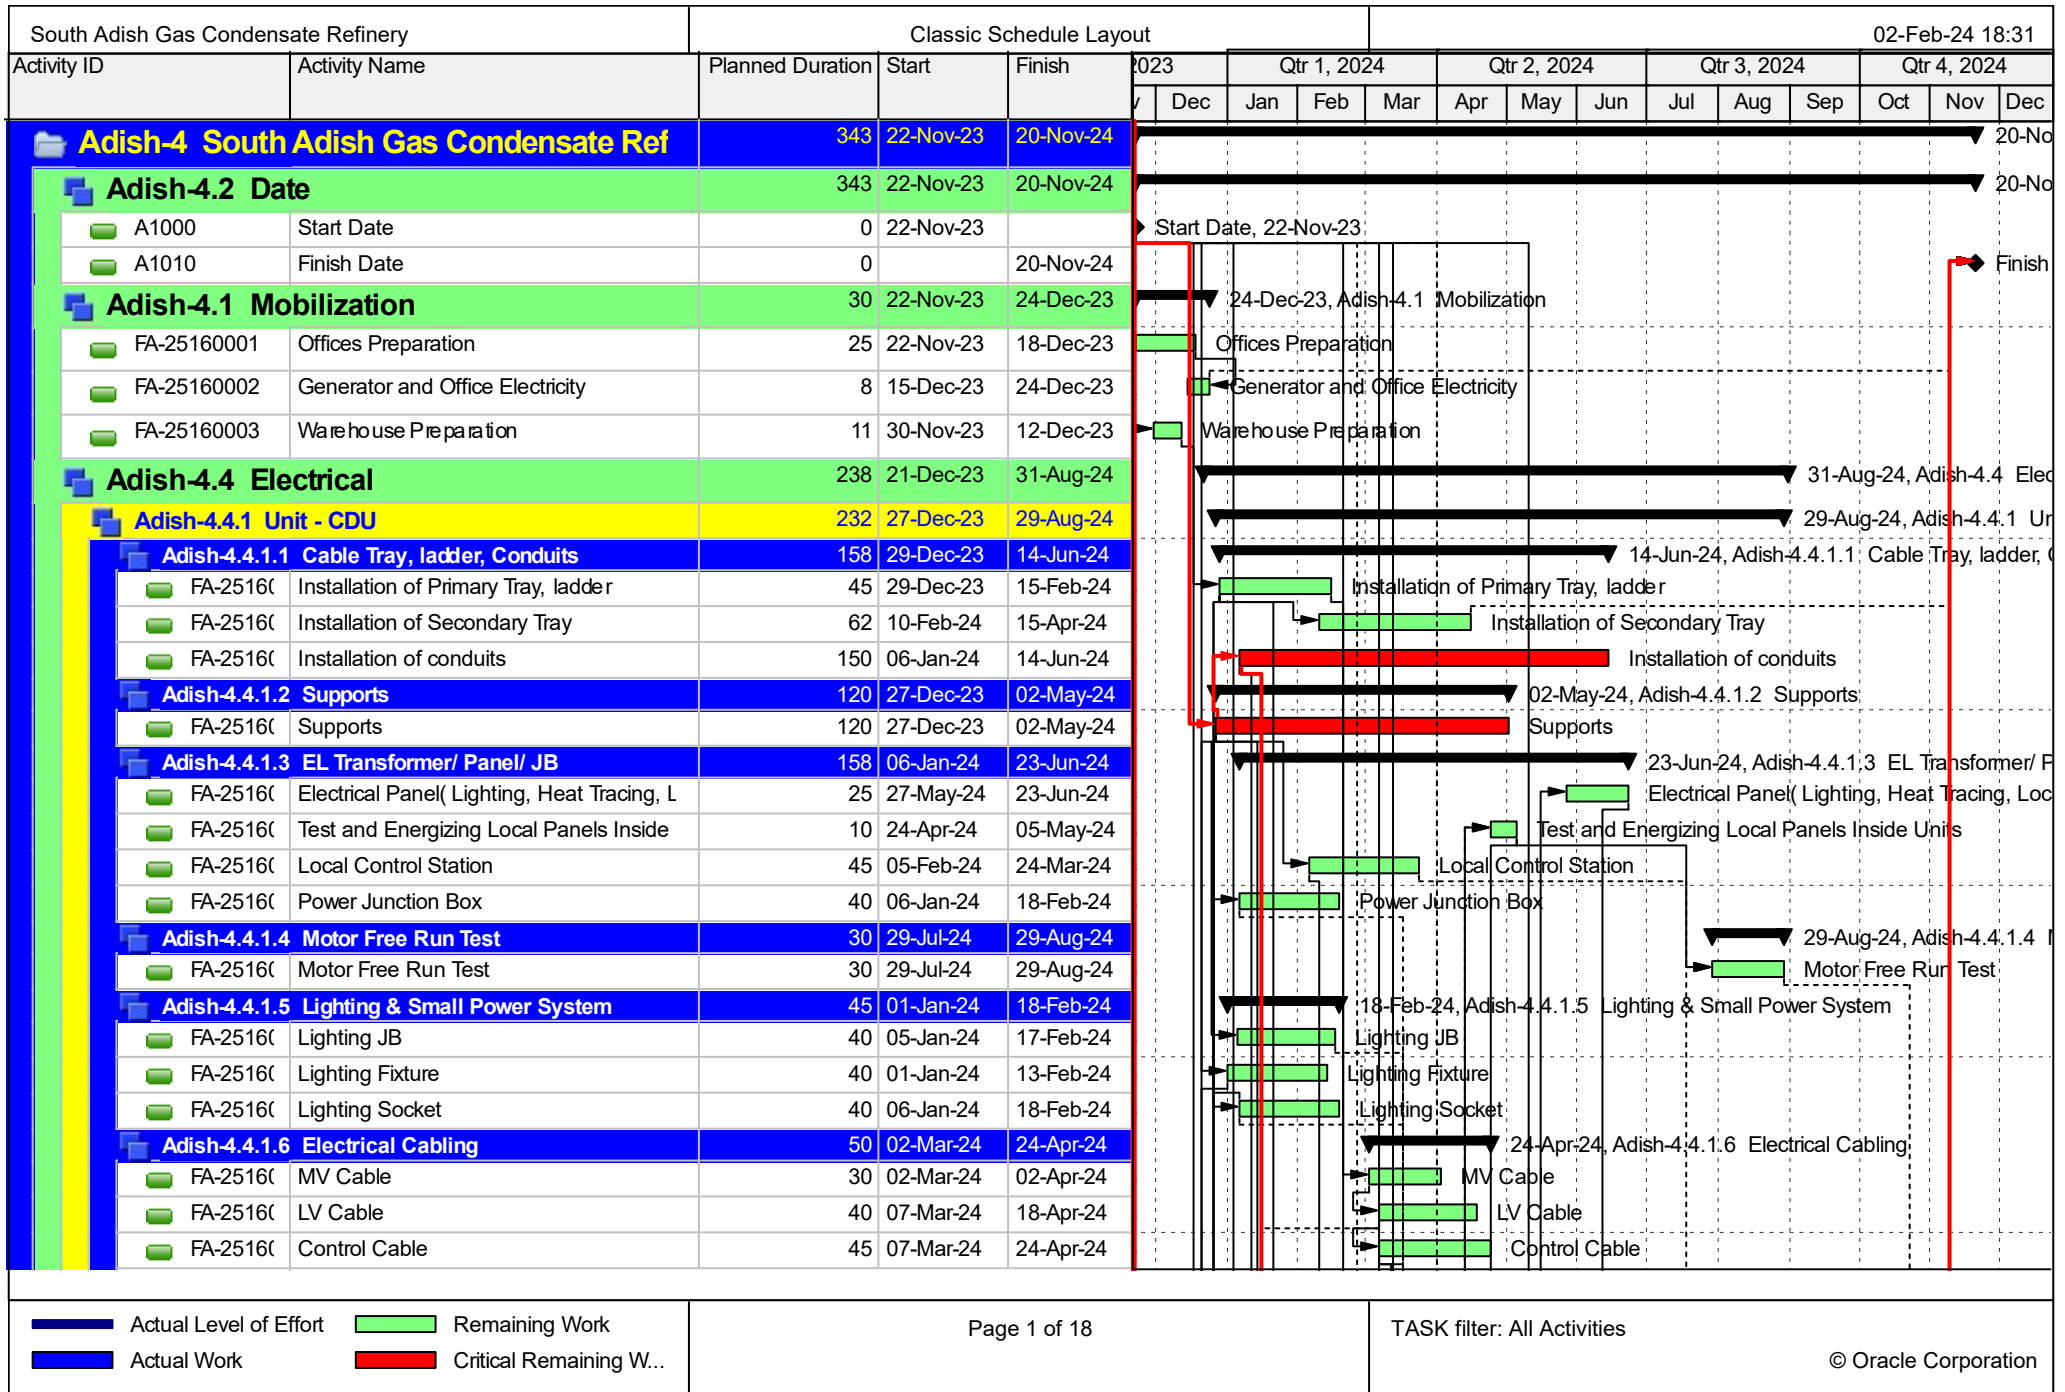


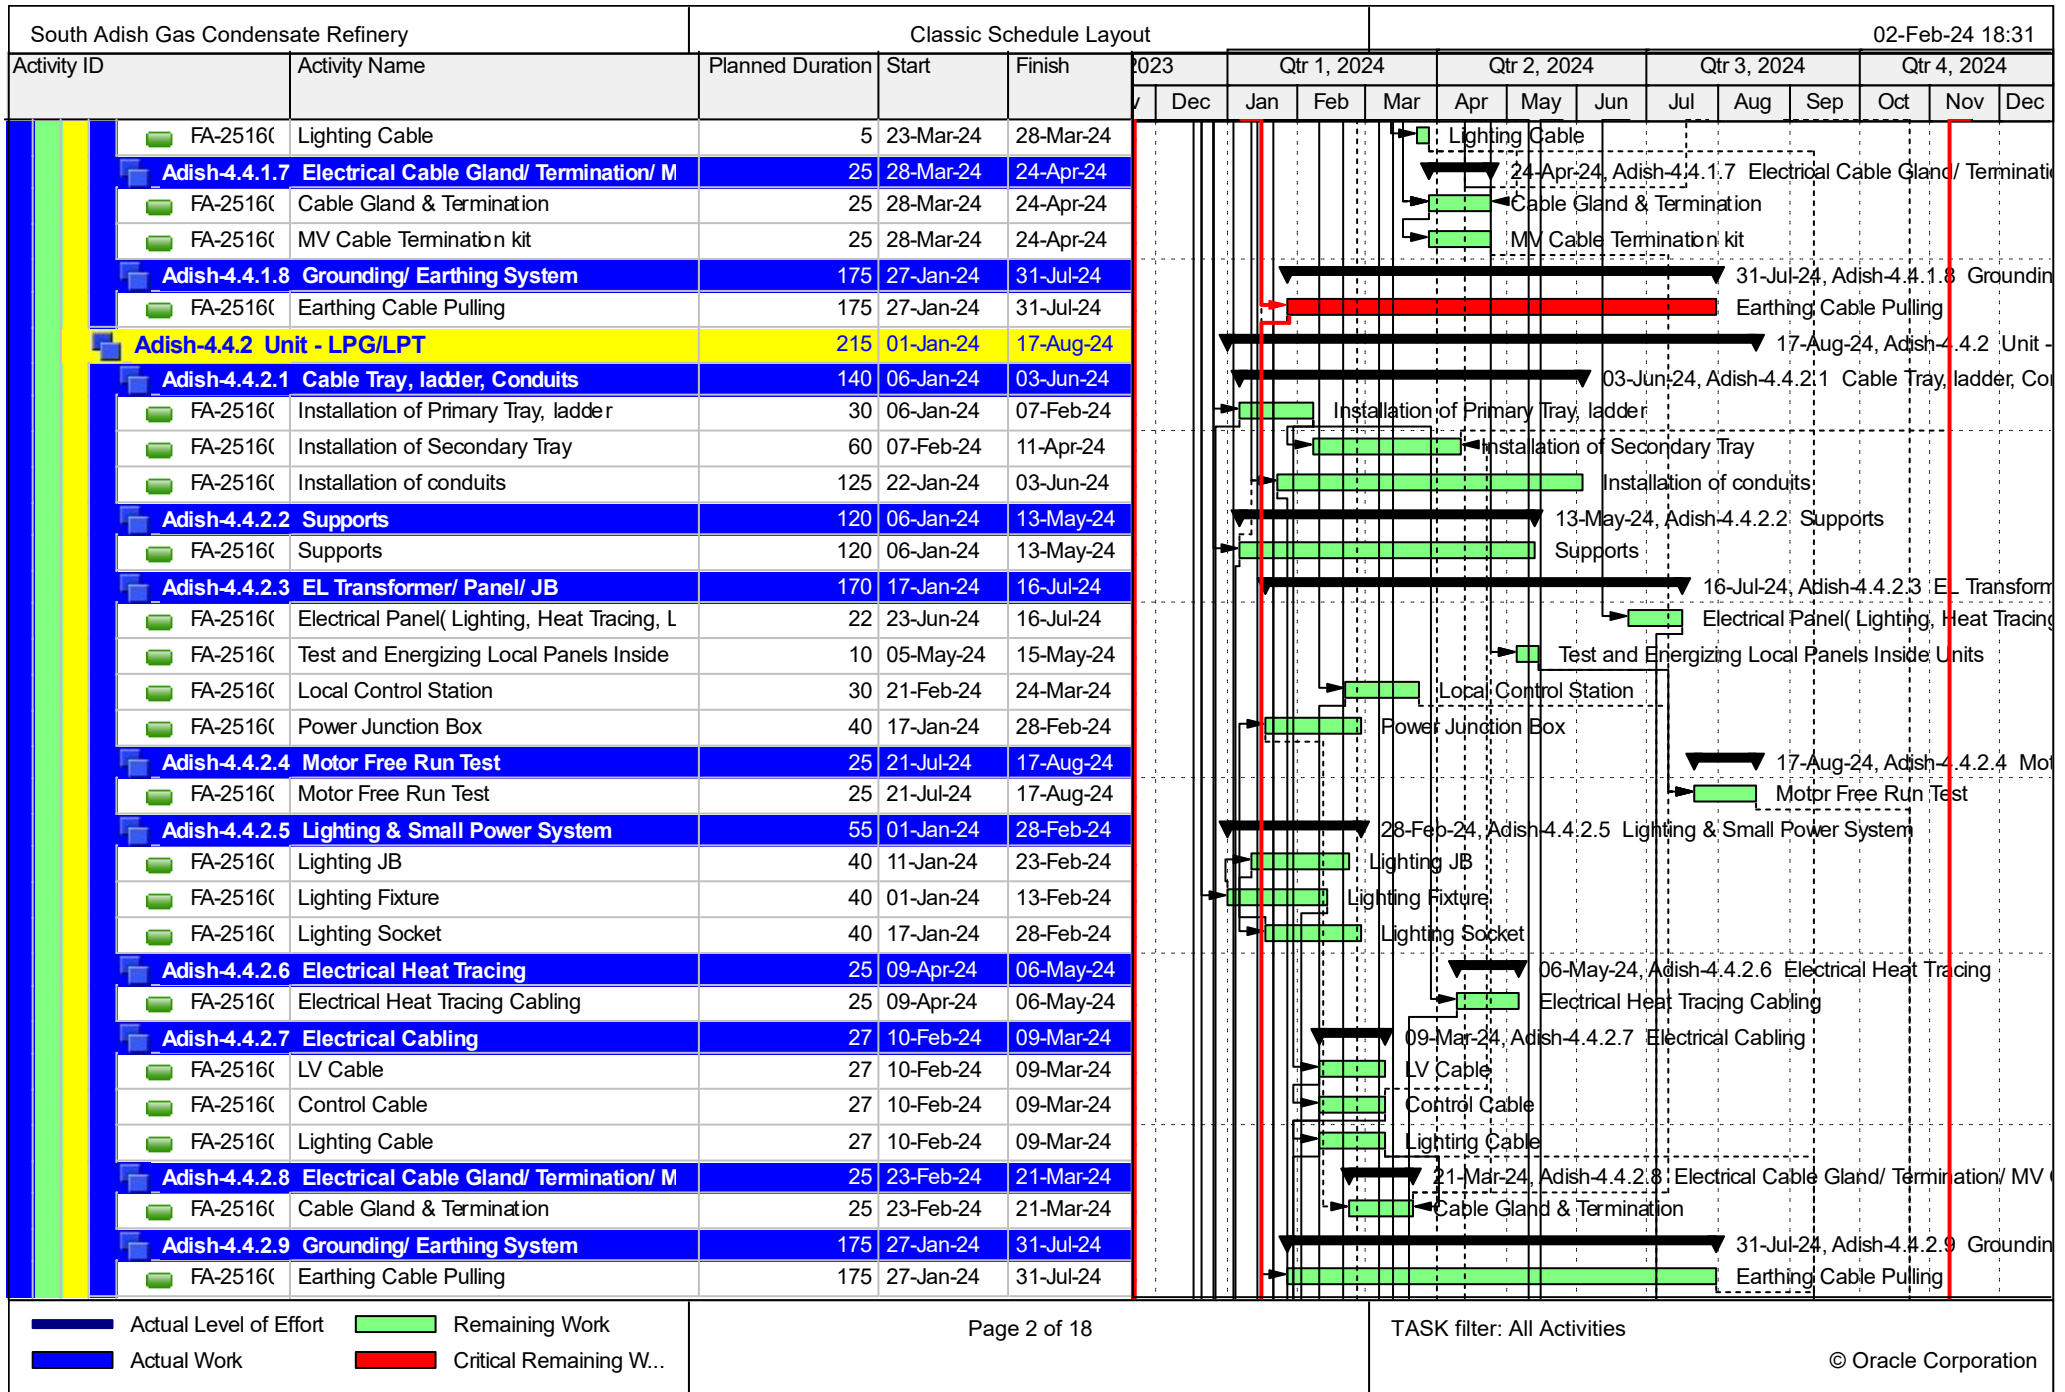


South Adish Gas Condensate Refinery			Classic Schedule Layout					02-Feb-24 18:31												
Activity ID		Activity Name	Planned Duration	Start	Finish	2023		Qtr 1, 2024				Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024		
						2023	2024	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	
Adish-4.4.4.2		Supports	90	15-Feb-24	20-May-24									20-May-24, Adish-4.4.4.2 Supports						
FA-2516C		Supports	90	15-Feb-24	20-May-24									Supports						
Adish-4.4.4.3		EL Transformer/ Panel/ JB	27	16-Mar-24	13-Apr-24									13-Apr-24, Adish-4.4.4.3 EL Transformer/ Panel/ JB						
FA-2516C		Electrical Panel(Lighting, Heat Tracing, L	18	16-Mar-24	03-Apr-24									Electrical Panel(Lighting, Heat Tracing, Local , ...)						
FA-2516C		Test and Energizing Local Panels Inside	18	20-Mar-24	08-Apr-24									Test and Energizing Local Panels Inside Units						
FA-2516C		Power Junction Box	25	18-Mar-24	13-Apr-24									Power Junction Box						
Adish-4.4.4.4		Motor Free Run Test	15	09-Jun-24	25-Jun-24									25-Jun-24, Adish-4.4.4.4 Motor Free Run Test						
FA-2516C		Motor Free Run Test	15	09-Jun-24	25-Jun-24									Motor Free Run Test						
Adish-4.4.4.5		Lighting & Small Power System	73	16-Feb-24	04-May-24									04-May-24, Adish-4.4.4.5 Lighting & Small Power System						
FA-2516C		Lighting JB	25	16-Feb-24	13-Mar-24									Lighting JB						
FA-2516C		Lighting Fixture	25	22-Mar-24	17-Apr-24									Lighting Fixture						
FA-2516C		Lighting Socket	25	07-Apr-24	04-May-24									Lighting Socket						
Adish-4.4.4.6		Electrical Cabling	27	01-Feb-24	29-Feb-24									29-Feb-24, Adish-4.4.4.6 Electrical Cabling						
FA-2516C		MV Cable	27	01-Feb-24	29-Feb-24									MV Cable						
FA-2516C		LV Cable	27	01-Feb-24	29-Feb-24									LV Cable						
FA-2516C		Control Cable	27	01-Feb-24	29-Feb-24									Control Cable						
FA-2516C		Lighting Cable	27	01-Feb-24	29-Feb-24									Lighting Cable						
Adish-4.4.4.7		Electrical Cable Gland/ Termination/ M	25	16-Feb-24	13-Mar-24									13-Mar-24, Adish-4.4.4.7 Electrical Cable Gland/ Termination/ MV Ca						
FA-2516C		Cable Gland & Termination	25	16-Feb-24	13-Mar-24									Cable Gland & Termination						
FA-2516C		MV Cable Termination kit	25	16-Feb-24	13-Mar-24									MV Cable Termination kit						
Adish-4.4.4.8		Grounding/ Earthing System	175	27-Jan-24	31-Jul-24									31-Jul-24, Adish-4.4.4.8 Grounding						
FA-2516C		Earthing Cable Pulling	175	27-Jan-24	31-Jul-24									Earthing Cable Pulling						
Adish-4.4.5		Unit - SWS	175	27-Jan-24	31-Jul-24									31-Jul-24, Adish-4.4.5 Unit - SWS						
Adish-4.4.5.1		Cable Tray, ladder, Conduits	114	20-Feb-24	20-Jun-24									20-Jun-24, Adish-4.4.5.1 Cable Tray, ladder						
FA-2516C		Installation of Primary Tray, ladder	30	06-Mar-24	07-Apr-24									Installation of Primary Tray, ladder						
FA-2516C		Installation of Secondary Tray	60	17-Apr-24	20-Jun-24									Installation of Secondary Tray						
FA-2516C		Installation of conduits	95	20-Feb-24	31-May-24									Installation of conduits						
Adish-4.4.5.2		Supports	90	15-Feb-24	20-May-24									20-May-24, Adish-4.4.5.2 Supports						
FA-2516C		Supports	90	15-Feb-24	20-May-24									Supports						
Adish-4.4.5.3		EL Transformer/ Panel/ JB	47	02-Mar-24	21-Apr-24									21-Apr-24, Adish-4.4.5.3 EL Transformer/ Panel/ JB						
FA-2516C		Electrical Panel(Lighting, Heat Tracing, L	15	04-Apr-24	20-Apr-24									Electrical Panel(Lighting, Heat Tracing, Local , ...)						
FA-2516C		Test and Energizing Local Panels Inside	10	10-Apr-24	21-Apr-24									Test and Energizing Local Panels Inside Units						
FA-2516C		Local Control Station	15	24-Mar-24	09-Apr-24									Local Control Station						
Actual Level of Effort Actual Work Remaining Work Critical Remaining W...																				
Page 4 of 18										TASK filter: All Activities										
© Oracle Corporation																				

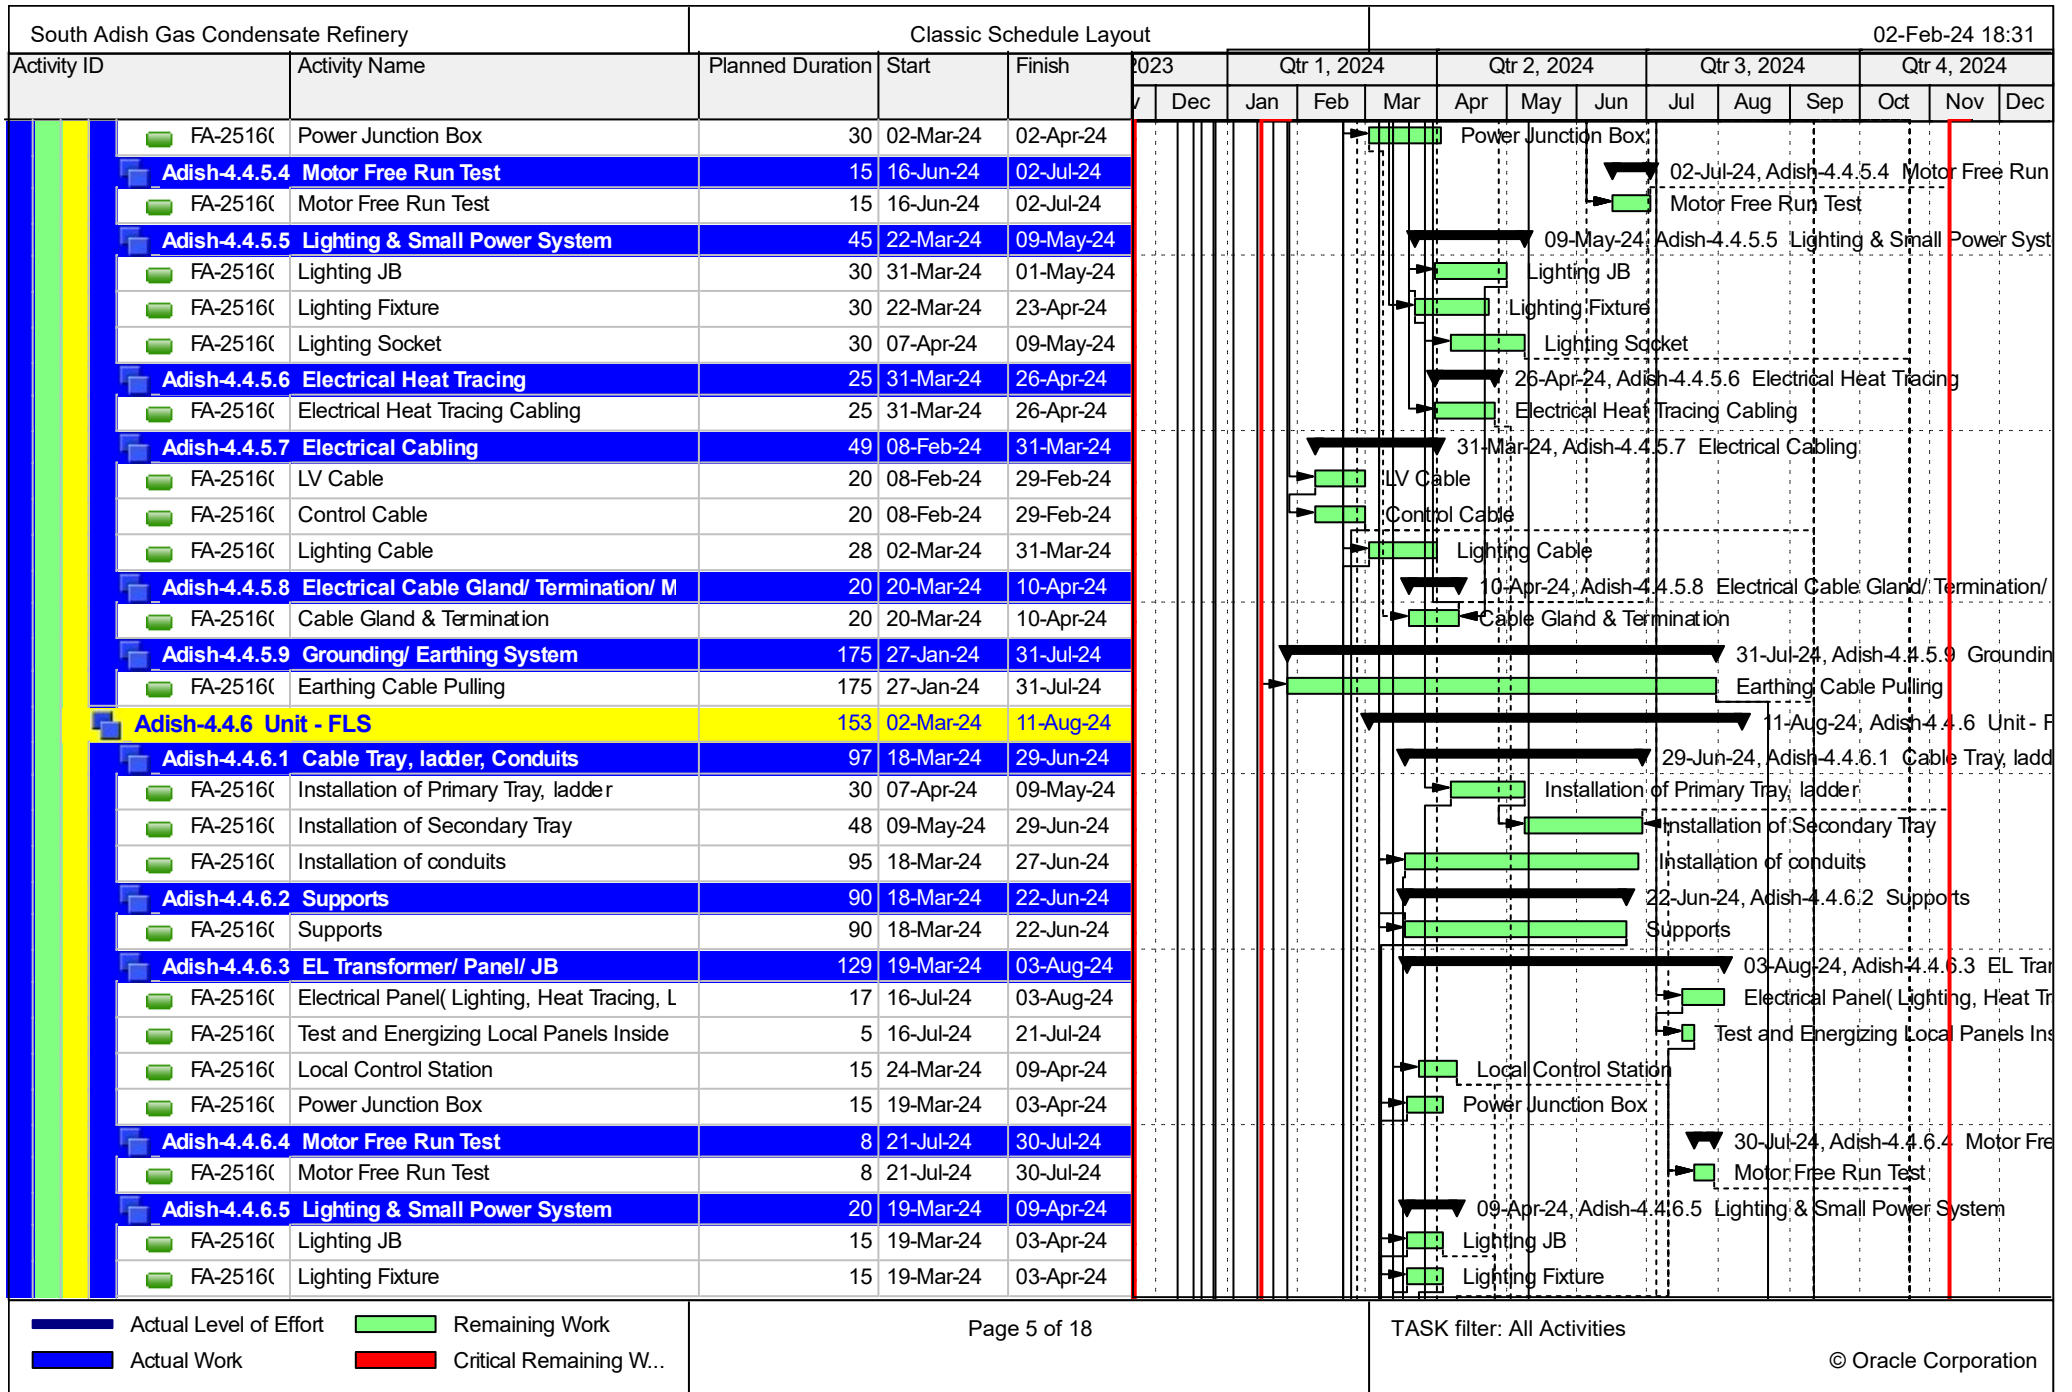


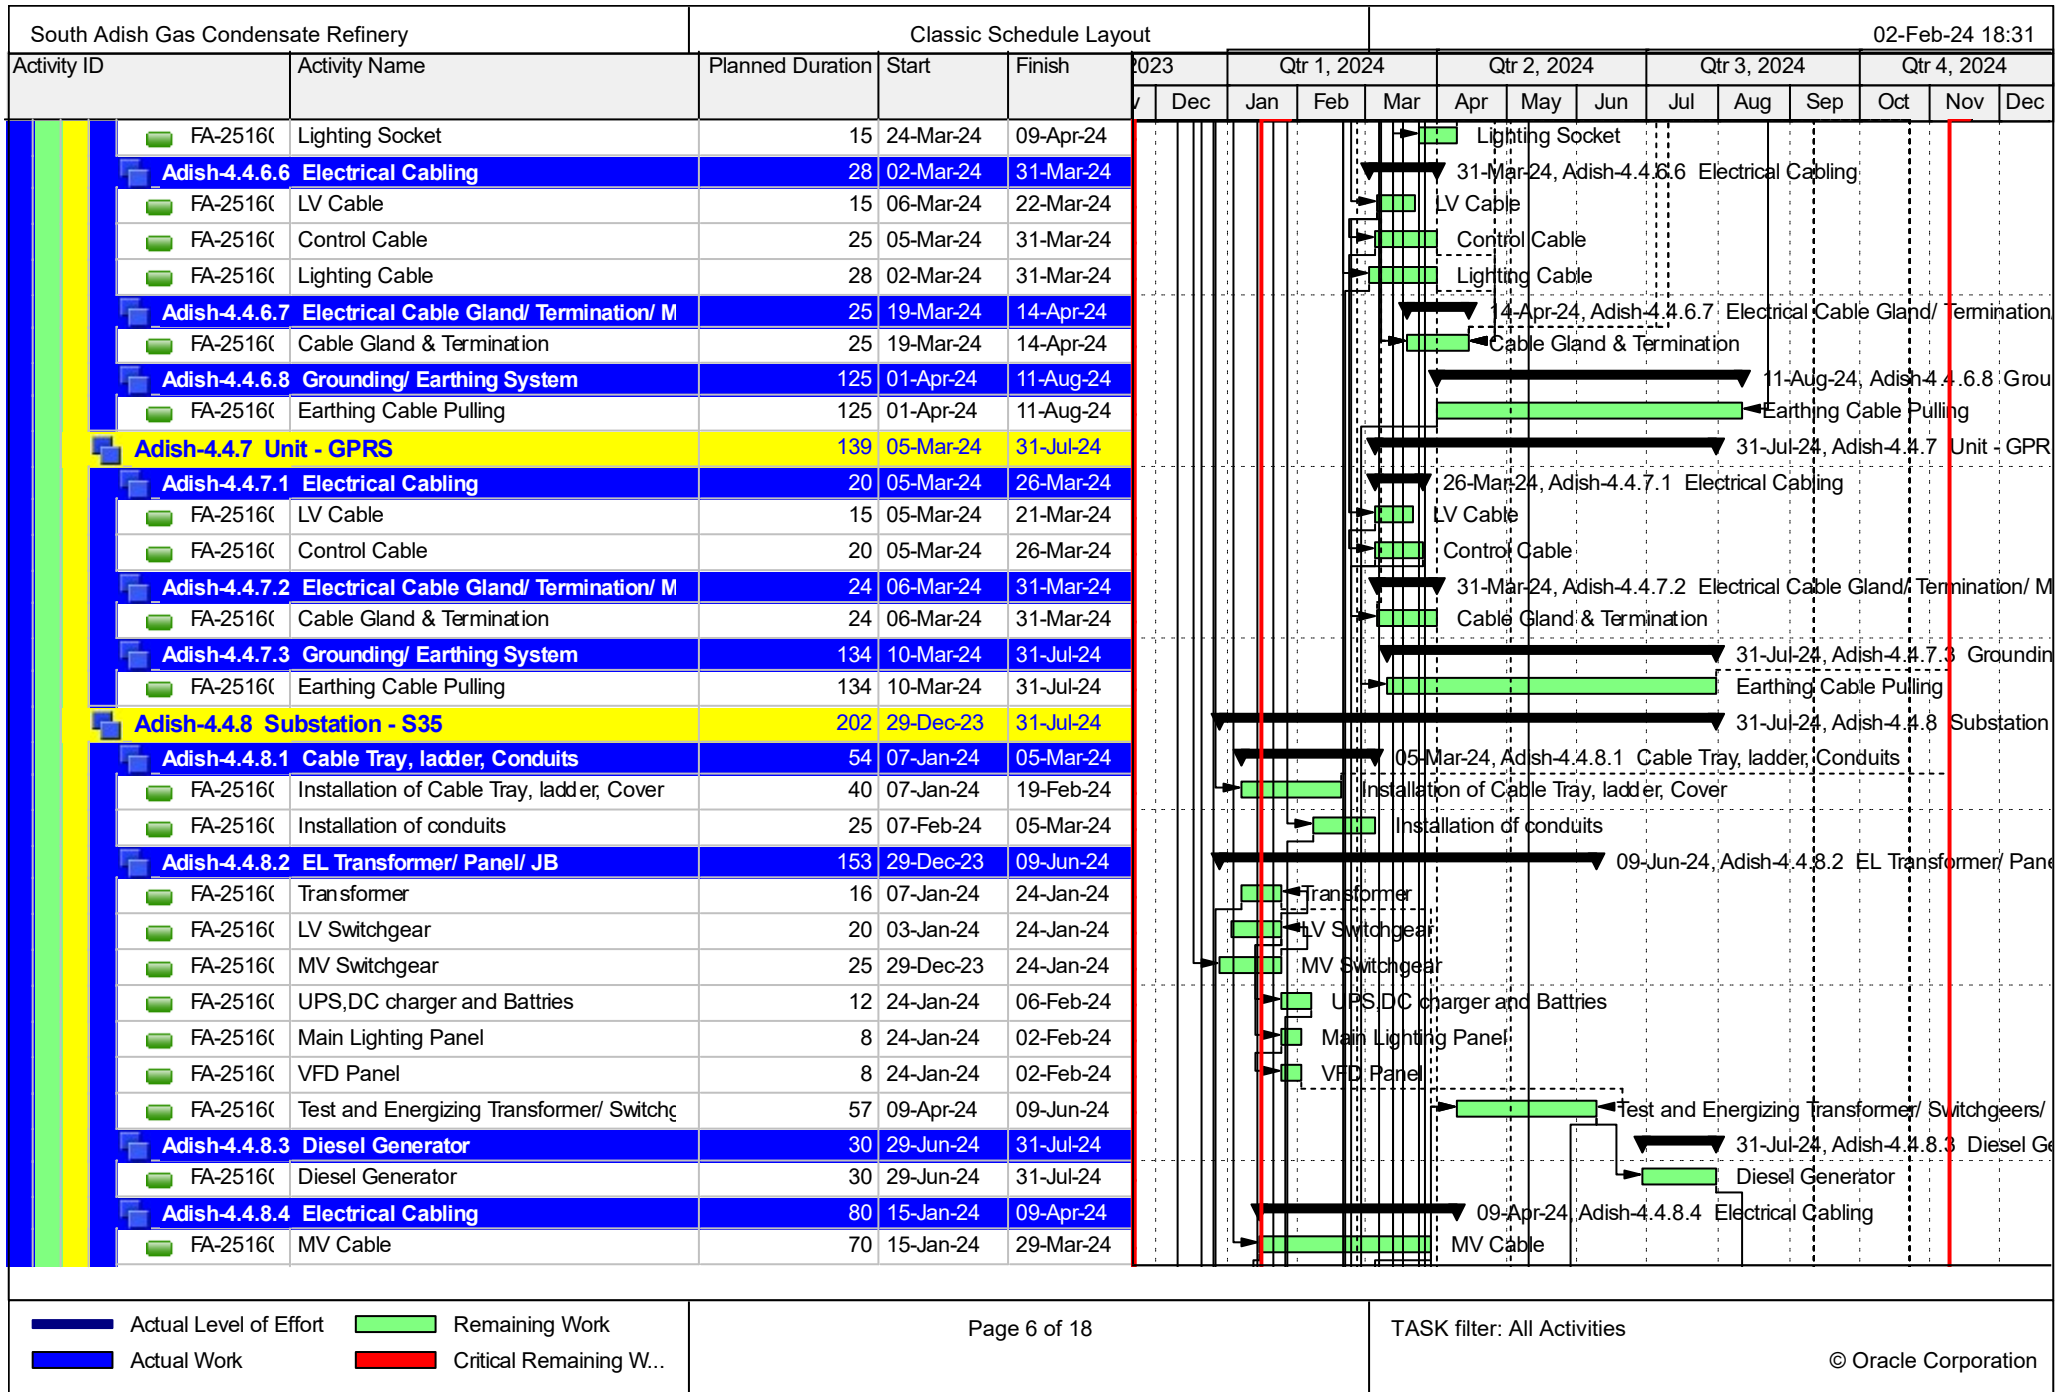

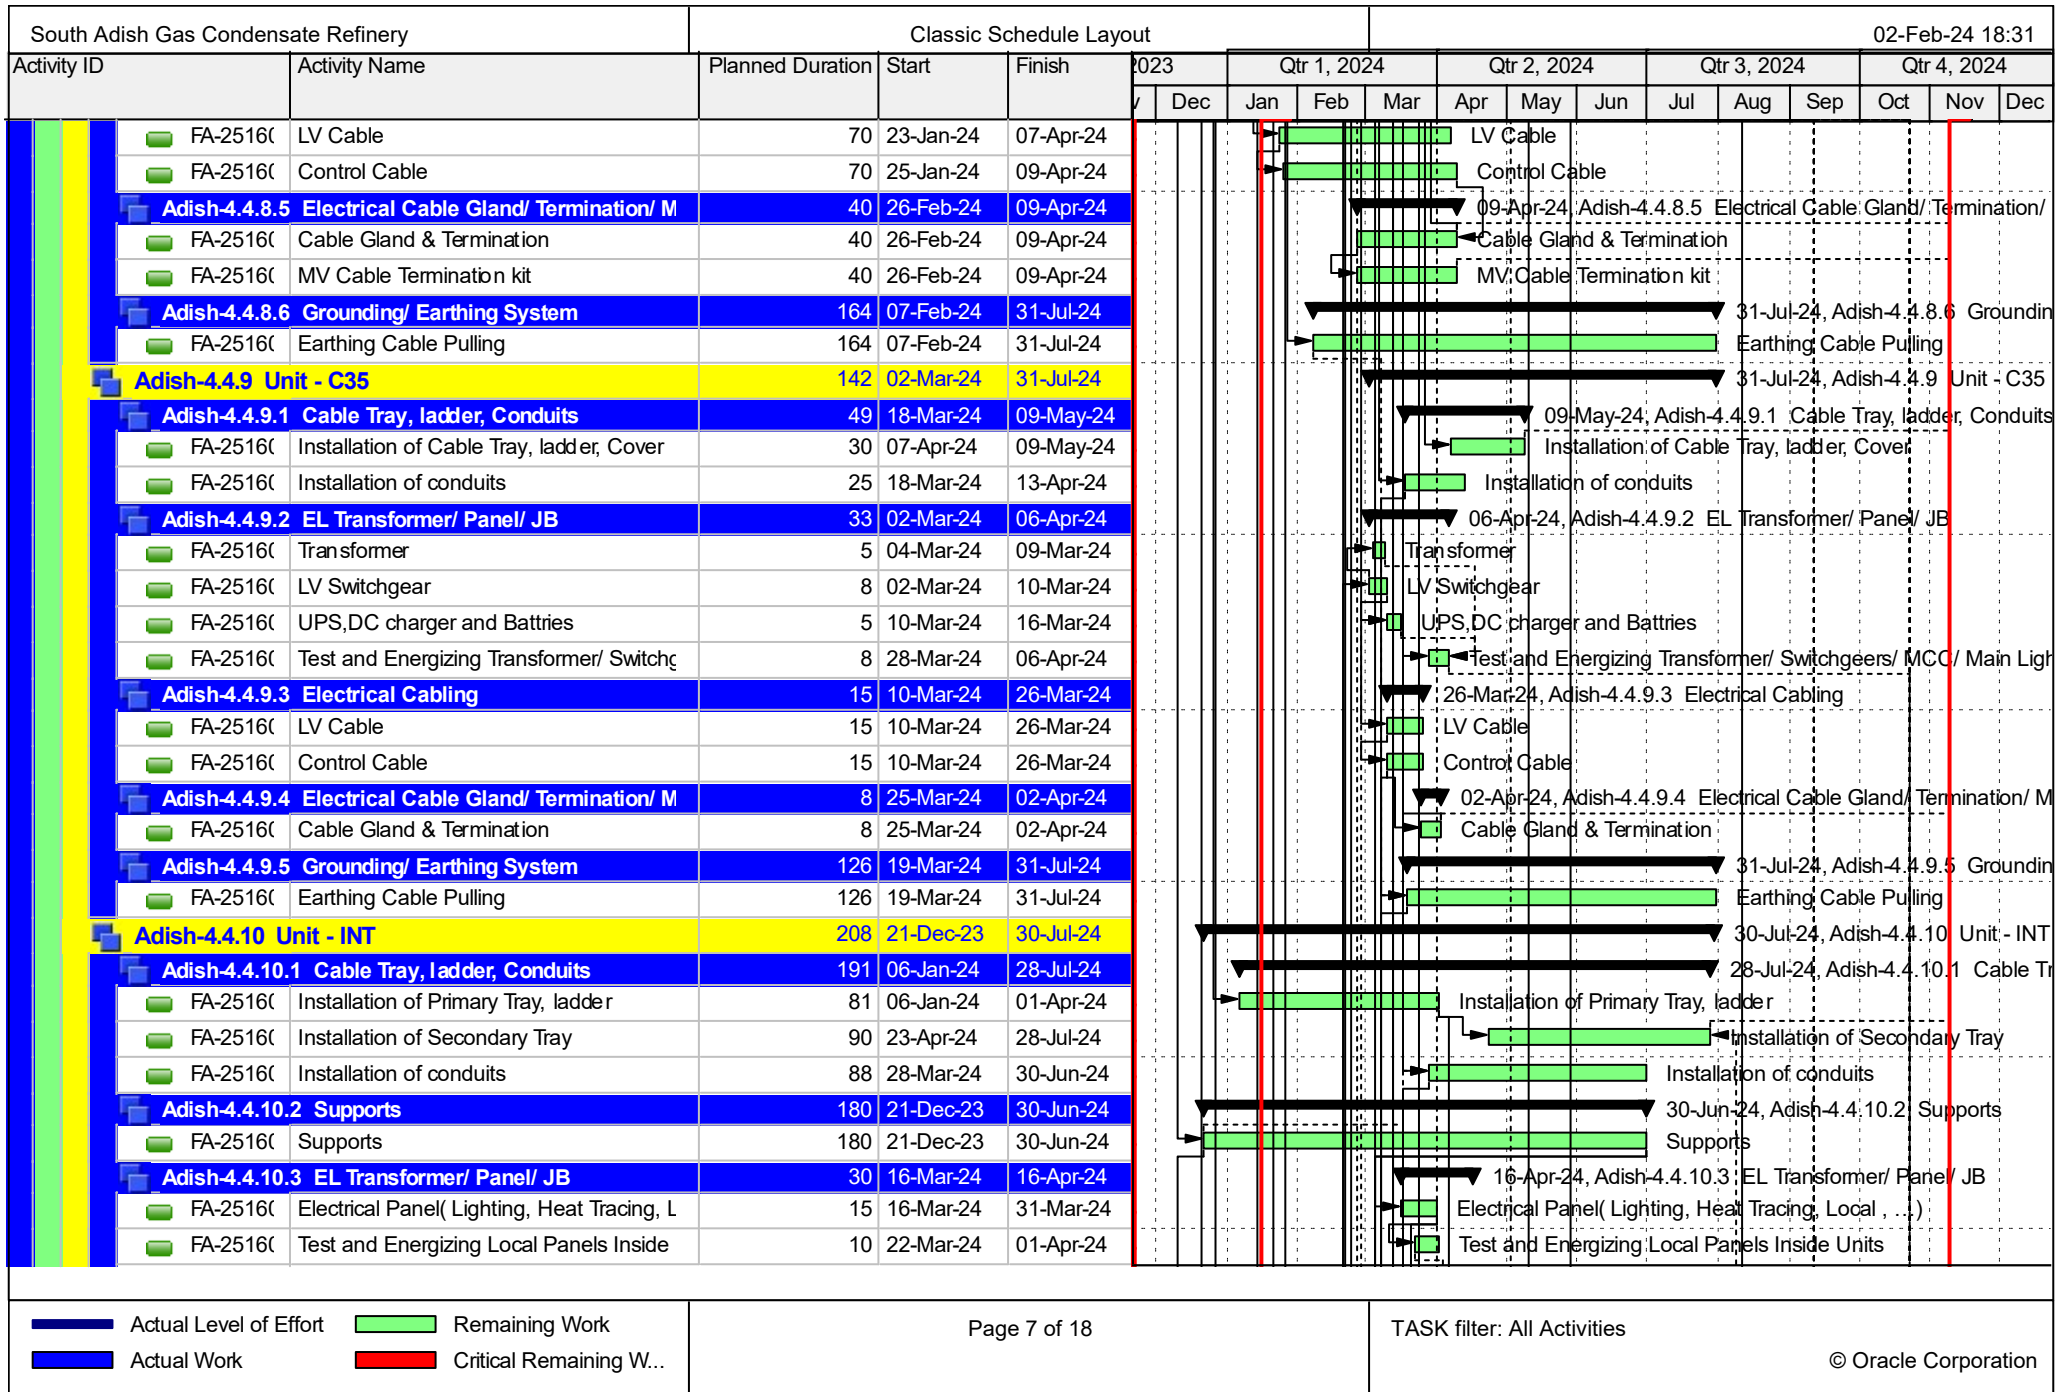

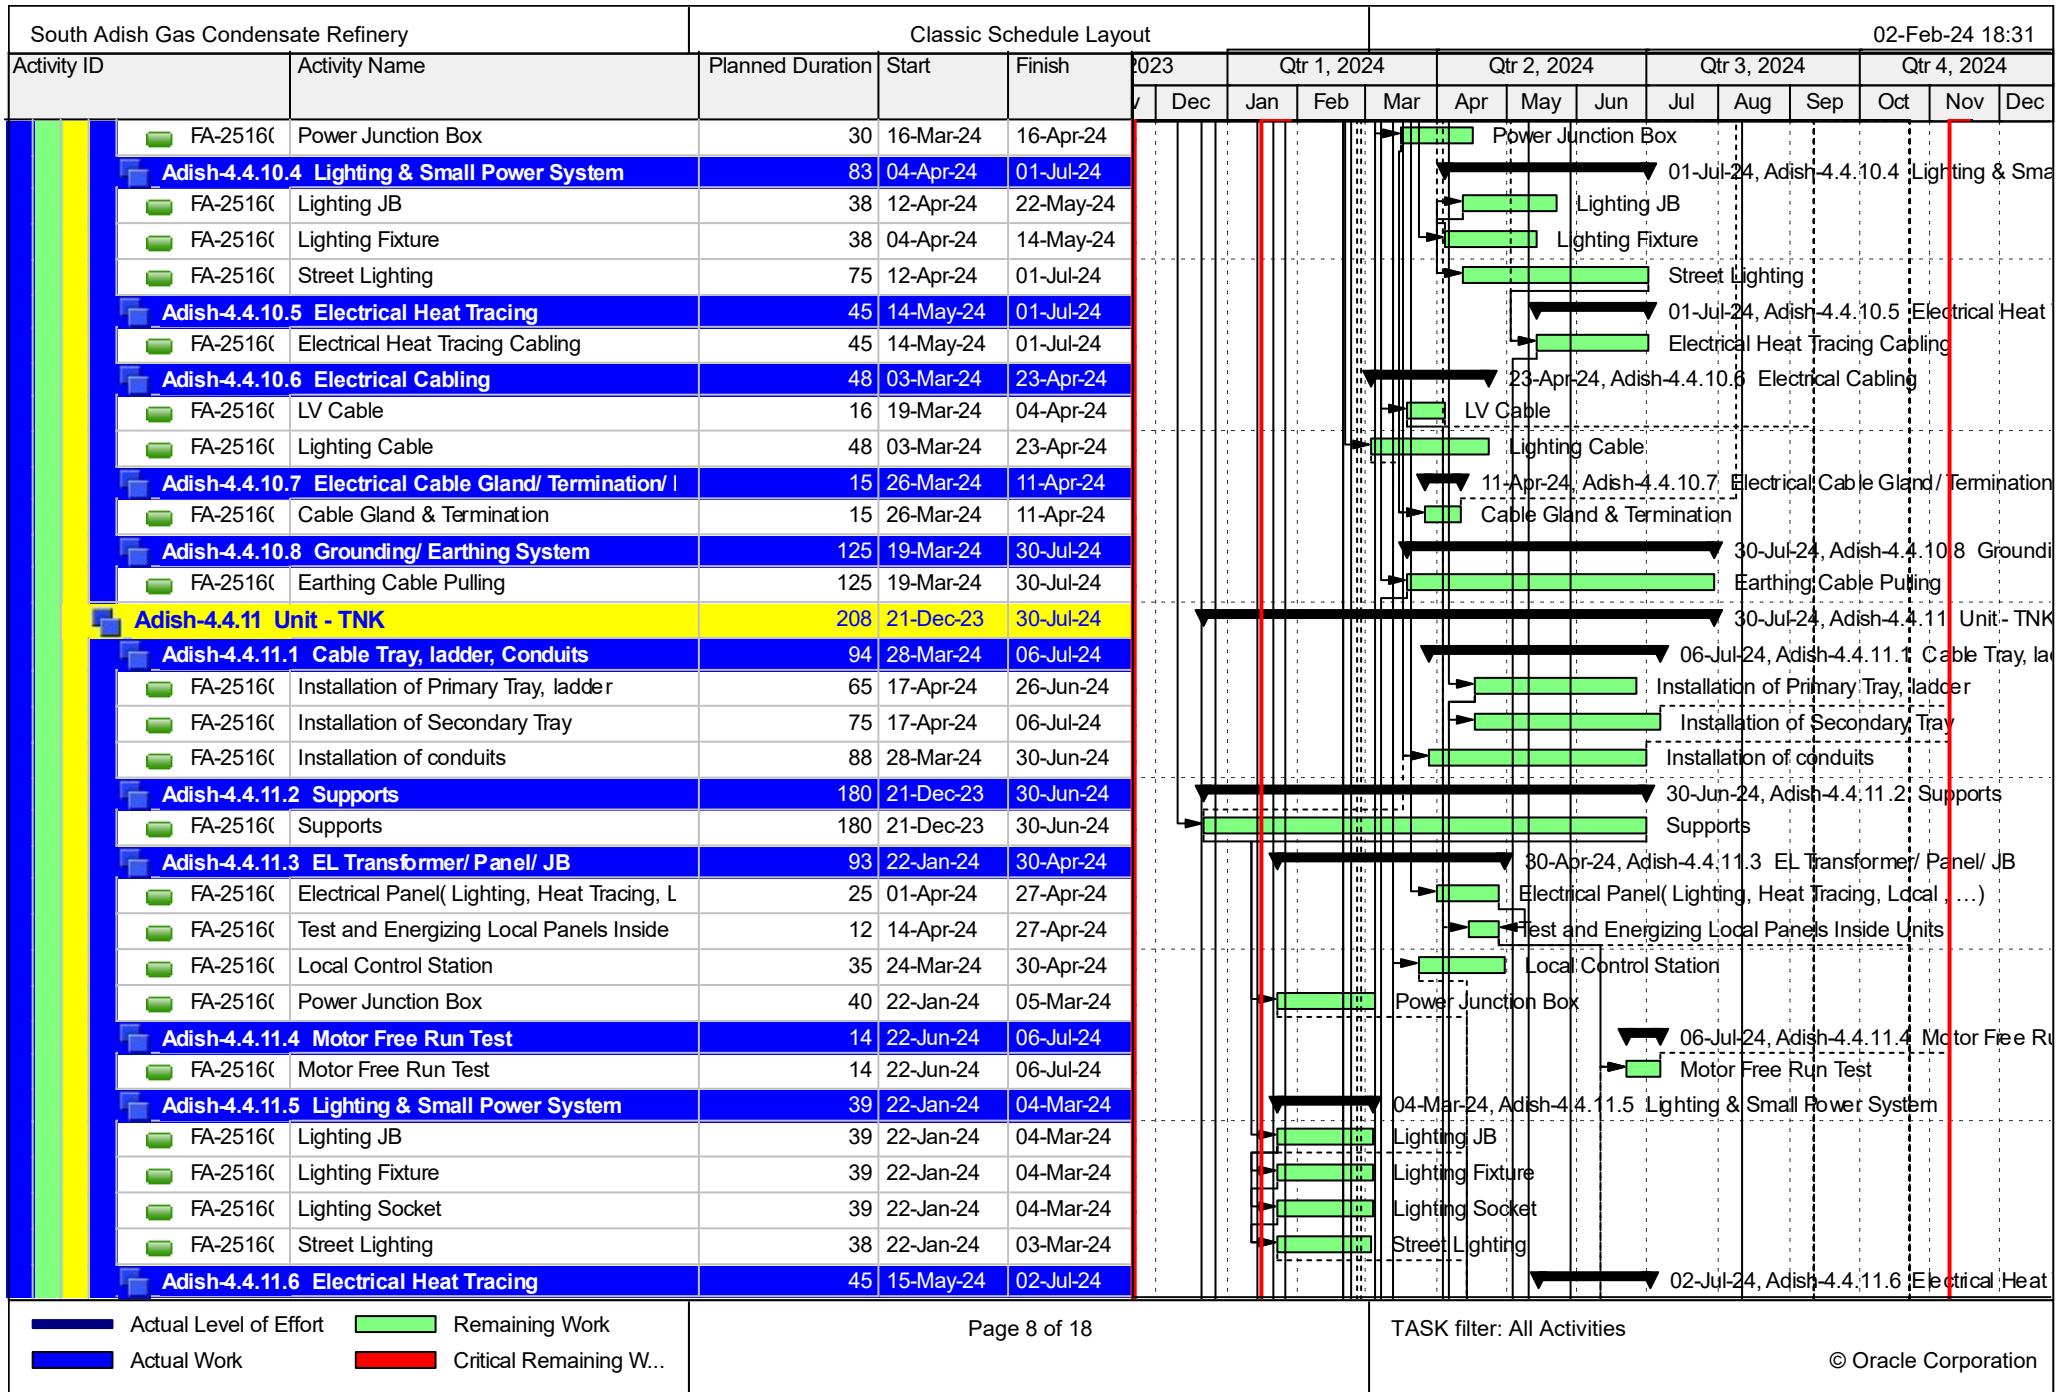

[illegible]

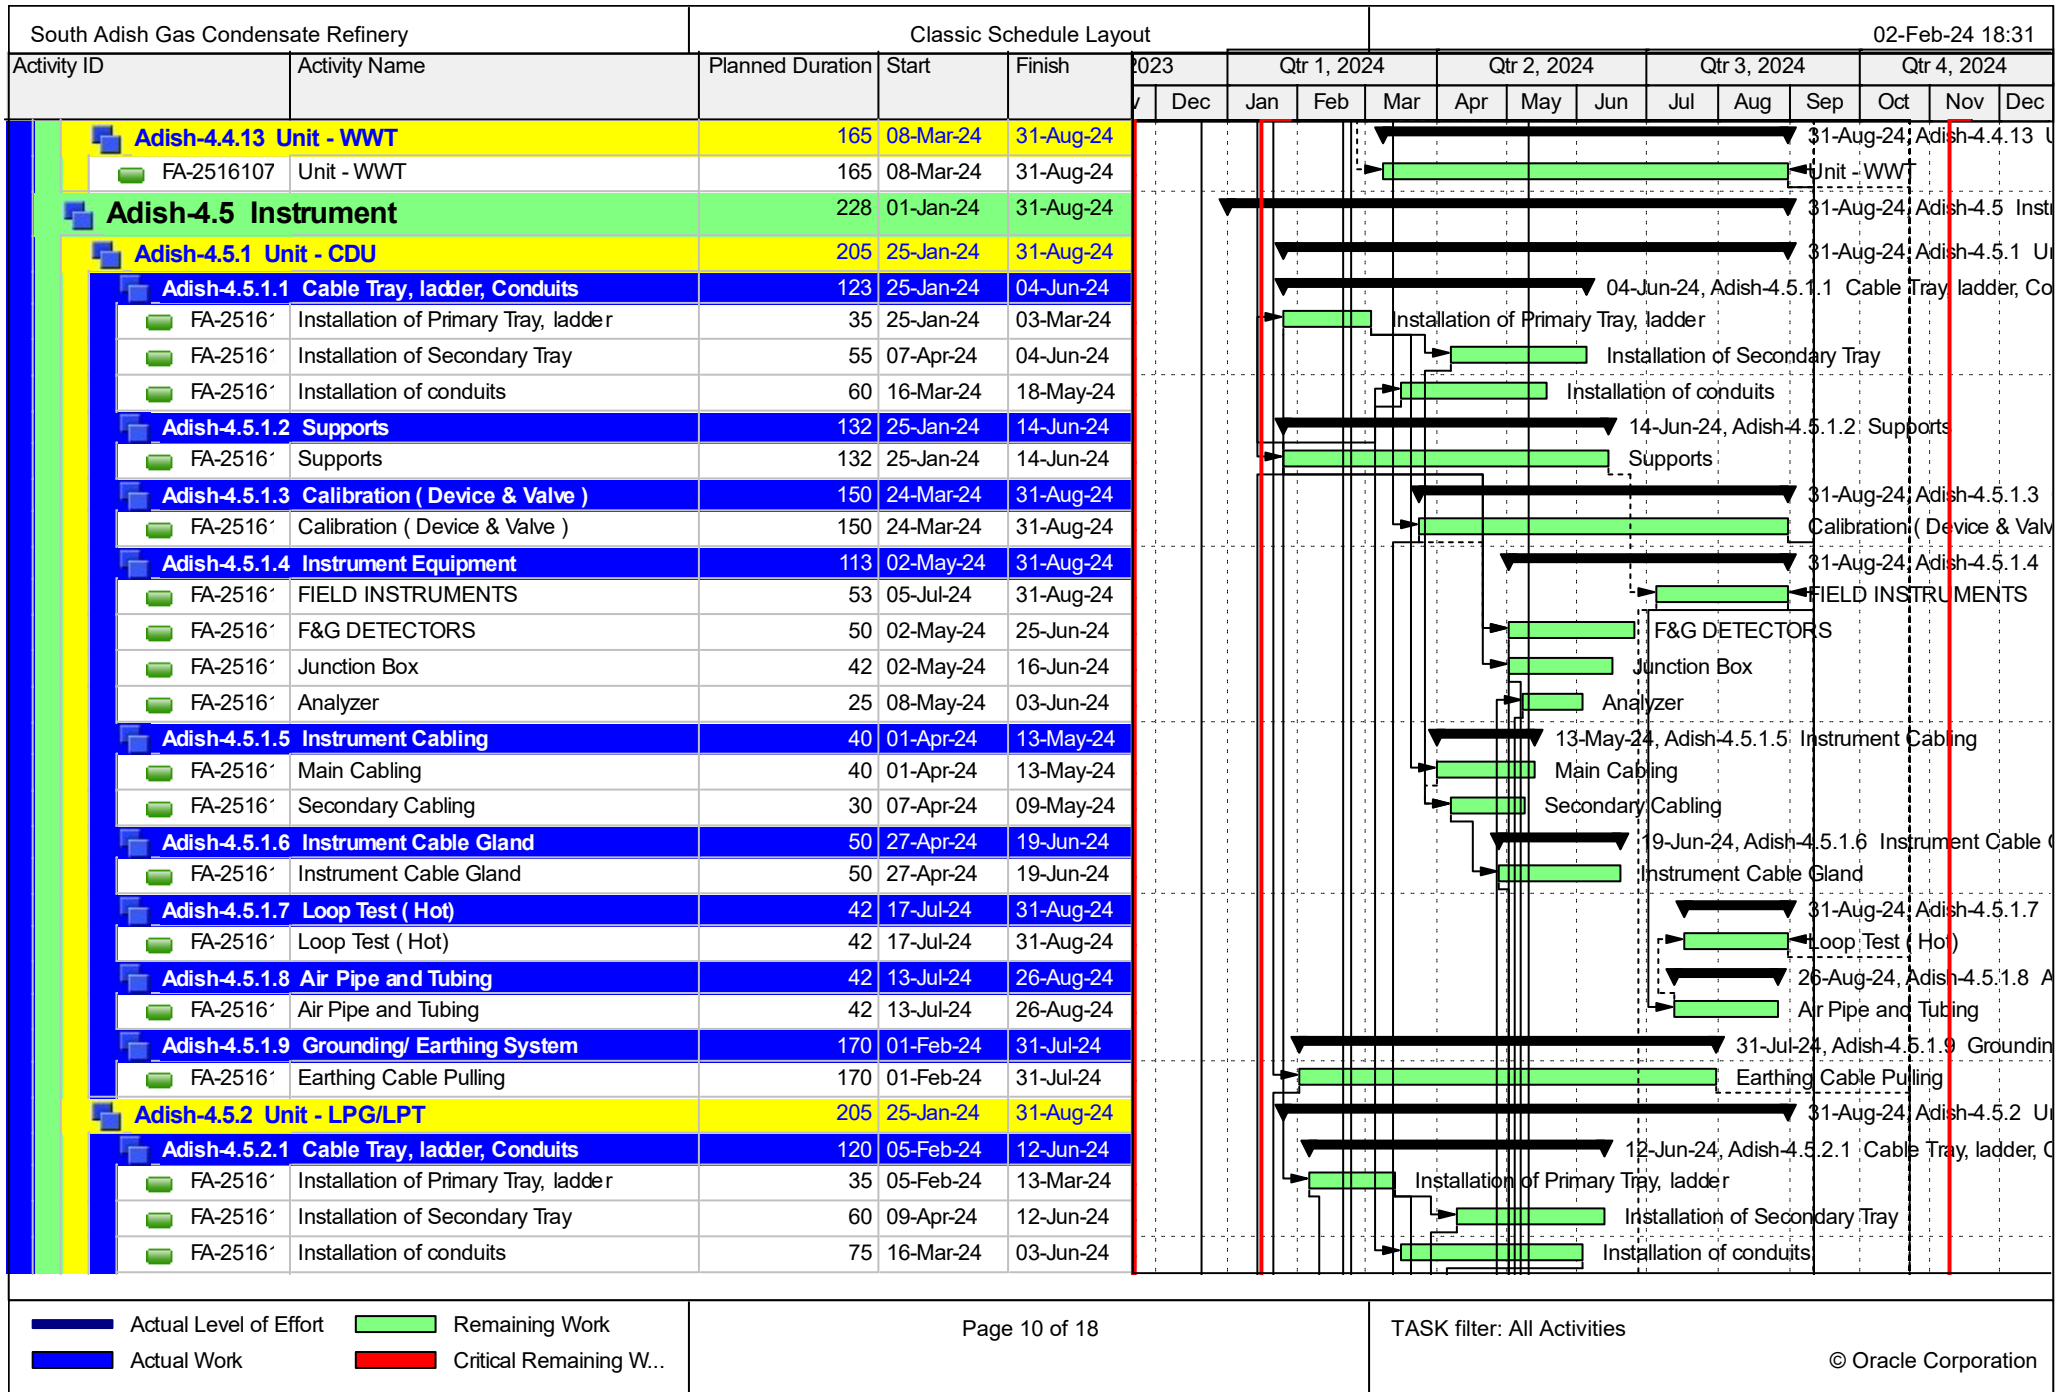

South Adish Gas Condensate Refinery			Classic Schedule Layout					02-Feb-24 18:31											
Activity ID		Activity Name	Planned Duration	Start	Finish	2023		Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024		
						Jan	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
	Adish-4.5.2.2 Supports		155	25-Jan-24	08-Jul-24										08-Jul-24, Adish-4.5.2.2 Supports				
	FA-2516	Supports	155	25-Jan-24	08-Jul-24										Supports				
	Adish-4.5.2.3 Calibration (Device & Valve)		150	24-Mar-24	31-Aug-24										31-Aug-24, Adish-4.5.2.3				
	FA-2516	Calibration (Device & Valve)	150	24-Mar-24	31-Aug-24										Calibration: (Device & Valve)				
	Adish-4.5.2.4 Instrument Equipment		103	13-May-24	31-Aug-24										31-Aug-24, Adish-4.5.2.4				
	FA-2516	FIELD INSTRUMENTS	50	08-Jul-24	31-Aug-24										FIELD INSTRUMENTS				
	FA-2516	F&G DETECTORS	50	13-May-24	05-Jul-24										F&G DETECTORS				
	FA-2516	Junction Box	42	18-May-24	02-Jul-24										Junction Box				
	FA-2516	Analyzer	25	16-May-24	12-Jun-24										Analyzer				
	Adish-4.5.2.5 Instrument Cabling		40	01-Apr-24	13-May-24										13-May-24, Adish-4.5.2.5 Instrument Cabling				
	FA-2516	Main Cabling	40	01-Apr-24	13-May-24										Main Cabling				
	FA-2516	Secondary Cabling	25	09-Apr-24	06-May-24										Secondary Cabling				
	Adish-4.5.2.6 Instrument Cable Gland		50	13-May-24	05-Jul-24										05-Jul-24, Adish-4.5.2.6 Instrument Cab				
	FA-2516	Instrument Cable Gland	50	13-May-24	05-Jul-24										Instrument Cable Gland				
	Adish-4.5.2.7 Loop Test (Hot)		40	19-Jul-24	31-Aug-24										31-Aug-24, Adish-4.5.2.7				
	FA-2516	Loop Test (Hot)	40	19-Jul-24	31-Aug-24										Loop Test (Hot)				
	Adish-4.5.2.8 Air Pipe and Tubing		50	08-Jul-24	31-Aug-24										31-Aug-24, Adish-4.5.2.8				
	FA-2516	Air Pipe and Tubing	50	08-Jul-24	31-Aug-24										Air Pipe and Tubing				
	Adish-4.5.2.9 Grounding/ Earthing System		170	01-Feb-24	31-Jul-24										31-Jul-24, Adish-4.5.2.9 Groundin				
	FA-2516	Earthing Cable Pulling	170	01-Feb-24	31-Jul-24										Earthing Cable Pulling				
	Adish-4.5.3 Unit - UTILITY		205	25-Jan-24	31-Aug-24										31-Aug-24, Adish-4.5.3 U				
	Adish-4.5.3.1 Cable Tray, ladder, Conduits		107	21-Feb-24	14-Jun-24										14-Jun-24, Adish-4.5.3.1 Cable Tray, ladder, C				
	FA-2516	Installation of Primary Tray, ladder	30	21-Feb-24	24-Mar-24										Installation of Primary Tray, ladder				
	FA-2516	Installation of Secondary Tray	55	16-Apr-24	14-Jun-24										Installation of Secondary Tray				
	FA-2516	Installation of conduits	30	16-Apr-24	18-May-24										Installation of conduits				
	Adish-4.5.3.2 Supports		155	25-Jan-24	08-Jul-24										08-Jul-24, Adish-4.5.3.2 Supports				
	FA-2516	Supports	155	25-Jan-24	08-Jul-24										Supports				
	Adish-4.5.3.3 Calibration (Device & Valve)		150	24-Mar-24	31-Aug-24										31-Aug-24, Adish-4.5.3.3				
	FA-2516	Calibration (Device & Valve)	150	24-Mar-24	31-Aug-24										Calibration (Device & Valve)				
	Adish-4.5.3.4 Instrument Equipment		93	23-May-24	31-Aug-24										31-Aug-24, Adish-4.5.3.4				
	FA-2516	FIELD INSTRUMENTS	50	08-Jul-24	31-Aug-24										FIELD INSTRUMENTS				
	FA-2516	F&G DETECTORS	50	23-May-24	16-Jul-24										F&G DETECTORS				
FA-2516	Junction Box	42	03-Jun-24	18-Jul-24										Junction Box					
FA-2516	Analyzer	25	03-Jun-24	30-Jun-24										Analyzer					

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining W...

Page 11 of 18

TASK filter: All Activities

© Oracle Corporation

South Adish Gas Condensate Refinery			Classic Schedule Layout					02-Feb-24 18:31													
Activity ID		Activity Name	Planned Duration	Start	Finish	2023		Qtr 1, 2024				Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			
						y	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec		
	Adish-4.5.3.5 Instrument Cabling		44	14-May-24	30-Jun-24									30-Jun-24, Adish-4.5.3.5 Instrument Cab							
	FA-2516'	Main Cabling	35	23-May-24	30-Jun-24									Main Cabling							
	FA-2516'	Secondary Cabling	25	14-May-24	10-Jun-24									Secondary Cabling							
	Adish-4.5.3.6 Instrument Cable Gland		35	23-May-24	30-Jun-24									30-Jun-24, Adish-4.5.3.6 Instrument Cab							
	FA-2516'	Instrument Cable Gland	35	23-May-24	30-Jun-24									Instrument Cable Gland							
	Adish-4.5.3.7 Loop Test (Hot)		25	04-Aug-24	31-Aug-24										31-Aug-24, Adish-4.5.3.7						
	FA-2516'	Loop Test (Hot)	25	04-Aug-24	31-Aug-24										Loop Test (Ho)						
	Adish-4.5.3.8 Air Pipe and Tubing		30	08-Jul-24	09-Aug-24										09-Aug-24, Adish-4.5.3.8 Air Pi						
	FA-2516'	Air Pipe and Tubing	30	08-Jul-24	09-Aug-24										Air Pipe and Tubing						
	Adish-4.5.3.9 Grounding/ Earthing System		170	01-Feb-24	31-Jul-24										31-Jul-24, Adish-4.5.3.9 Groundin						
	FA-2516'	Earthing Cable Pulling	170	01-Feb-24	31-Jul-24										Earthing Cable Pulling						
	Adish-4.5.4 Unit - FWS		205	25-Jan-24	31-Aug-24										31-Aug-24, Adish-4.5.4 Ui						
	Adish-4.5.4.1 Cable Tray, ladder, Conduits		83	08-Mar-24	04-Jun-24										04-Jun-24, Adish-4.5.4.1 Cable Tray ladder, Co						
	FA-2516'	Installation of Primary Tray, ladder	30	08-Mar-24	09-Apr-24										Installation of Primary Tray, ladder						
	FA-2516'	Installation of Secondary Tray	35	09-Apr-24	16-May-24										Installation of Secondary Tray						
	FA-2516'	Installation of conduits	32	01-May-24	04-Jun-24										Installation of conduits						
	Adish-4.5.4.2 Supports		145	25-Jan-24	28-Jun-24										28-Jun-24, Adish-4.5.4.2 Supports						
	FA-2516'	Supports	145	25-Jan-24	28-Jun-24										Supports						
	Adish-4.5.4.3 Calibration (Device & Valve)		48	10-Jul-24	31-Aug-24										31-Aug-24, Adish-4.5.4.3						
	FA-2516'	Calibration (Device & Valve)	48	10-Jul-24	31-Aug-24										Calibration (Device & Valv						
	Adish-4.5.4.4 Instrument Equipment		85	01-Jun-24	31-Aug-24										31-Aug-24, Adish-4.5.4.4						
	FA-2516'	FIELD INSTRUMENTS	35	24-Jul-24	31-Aug-24										FIELD INSTRUMENTS						
	FA-2516'	F&G DETECTORS	35	01-Jun-24	08-Jul-24										F&G DETECTORS						
	FA-2516'	Junction Box	30	06-Jun-24	08-Jul-24										Junction Box						
	FA-2516'	Analyzer	25	03-Jun-24	30-Jun-24										Analyzer						
	Adish-4.5.4.5 Instrument Cabling		22	08-Jun-24	01-Jul-24										01-Jul-24, Adish-4.5.4.5 Instrument Cabi						
	FA-2516'	Main Cabling	15	08-Jun-24	24-Jun-24										Main Cabling						
	FA-2516'	Secondary Cabling	20	10-Jun-24	01-Jul-24										Secondary Cabling						
Adish-4.5.4.6 Instrument Cable Gland		25	18-Jun-24	15-Jul-24										15-Jul-24, Adish-4.5.4.6 Instrument C							
FA-2516'	Instrument Cable Gland	25	18-Jun-24	15-Jul-24										Instrument Cable Gland							
Adish-4.5.4.7 Loop Test (Hot)		20	10-Aug-24	31-Aug-24										31-Aug-24, Adish-4.5.4.7							
FA-2516'	Loop Test (Hot)	20	10-Aug-24	31-Aug-24										Loop Test (Ho)							
Adish-4.5.4.8 Air Pipe and Tubing		25	04-Aug-24	31-Aug-24										31-Aug-24, Adish-4.5.4.8							
FA-2516'	Air Pipe and Tubing	25	04-Aug-24	31-Aug-24										Air Pipe and Tubing							

Actual Level of Effort

Remaining Work

Actual Work

Critical Remaining W...

Page 12 of 18

TASK filter: All Activities

© Oracle Corporation

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining W...

[illegible]

